



# Fort Wayne Riverfront Phase 1

Park Foundation Pavilion



**Riverfront**  
FORT WAYNE  
Always moving.

## Weekly Progress Update for Week Ending 7/1/18

### Past Two Weeks of Progress

- |   |   |
|---|---|
| <ul style="list-style-type: none"> <li>* Continue Metal Stud Framing for Canopy Soffit</li> <li>* Continue Pipe/Duct Insulation</li> <li>* Install Ice and Water Shield above Limestone Cladding for Pre-Finished Flashing</li> <li>* Continue Prime/Paint Interior Walls</li> <li>* Electrical Ceiling Rough-In</li> </ul> | <ul style="list-style-type: none"> <li>* Continue Metal Stud Framing Throughout Pavilion (Event Space Ceiling/Vestibule)</li> <li>* Continue Installation of Furring at Canopy Soffit</li> <li>* Install Plywood Sheathing/Rigid Foam Board Insulation at Metal Wall System Detail</li> <li>* Continue Installation of Pre-Finished Fascia</li> </ul> |
|---|---|


### Next Week Look Ahead

- |   |   |
|---|---|
| <ul style="list-style-type: none"> <li>* Continue Metal Stud Framing for Canopy Soffit</li> <li>* Install Ice and Water Shield above Limestone Cladding for Pre-Finished Flashing</li> <li>* Fill Interior of OHD Jambes and Headers with SPUF</li> </ul> | <ul style="list-style-type: none"> <li>* Continue Metal Stud Framing Throughout Pavilion (Event Space Ceiling/Vestibule)</li> <li>* Install Plywood Sheathing/Rigid Foam Board Insulation at Metal Wall System Detail</li> <li>* Continue Installation of Furring at Canopy Soffit</li> </ul> |
|---|---|

### Milestone Events

- \* Week of 7/23 Start Glazed Aluminum Curtain Walls

### Progress Photos

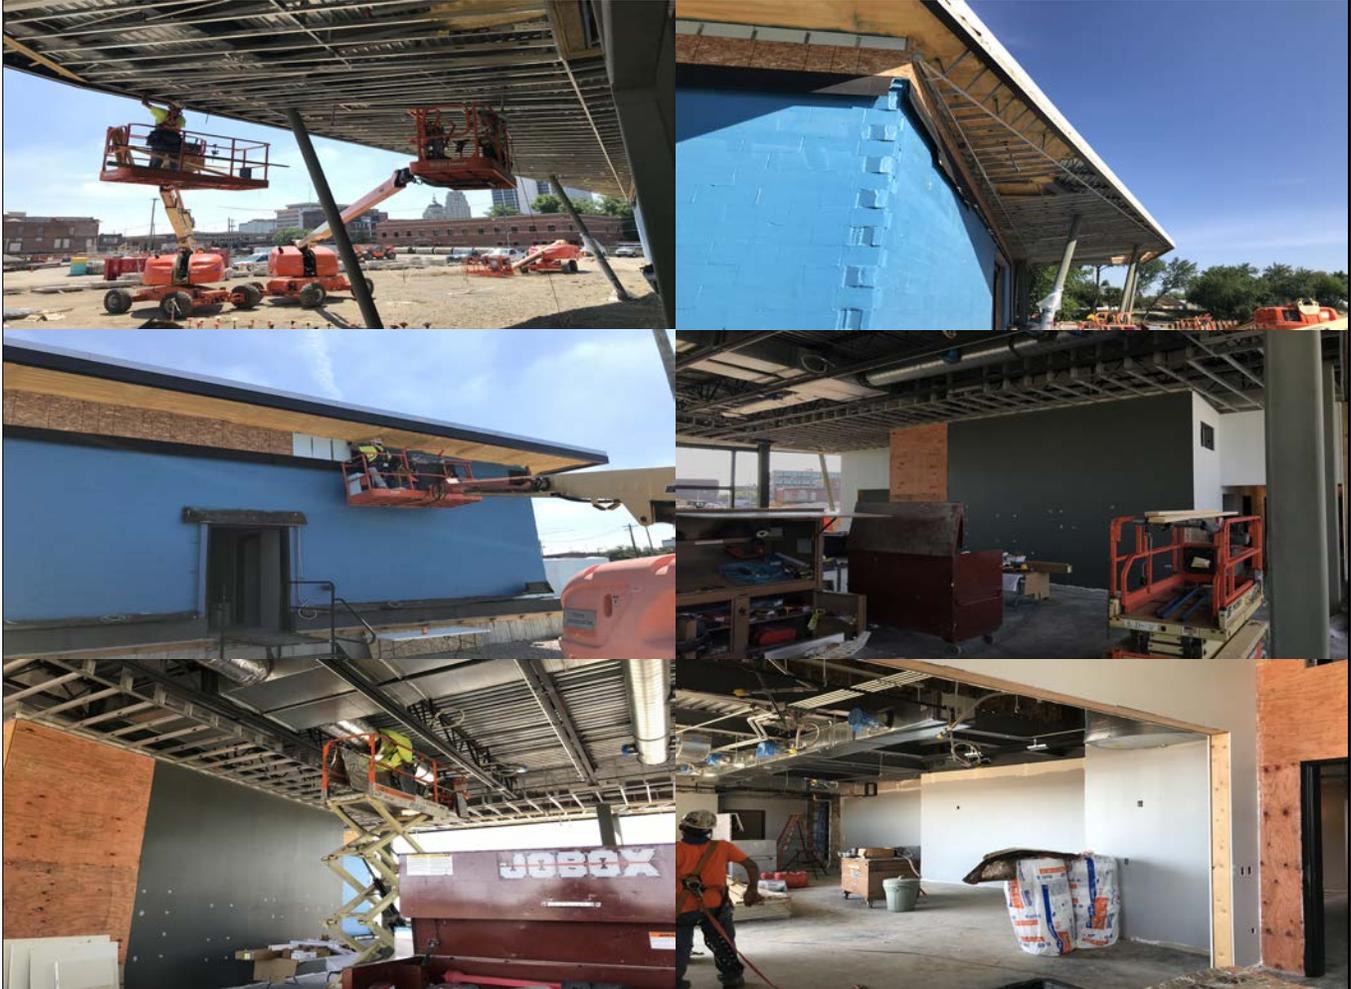



# Fort Wayne Riverfront Phase 1

## River Work North/South Shore & Misc. Site Excavation



### Weekly Progress Update for Week Ending 7/1/18

#### Past Two Weeks of Progress

- |  |   |
|--|---|
| <ul style="list-style-type: none"> <li>* Continue Driving H-Piles at South Shore Seawall (Vertical/Battered)</li> <li>* Continue Excavation Within North Shore Seawall Cofferdam</li> <li>* Continue Installation of Sheet Pile Bracing at North Seawall Cofferdam</li> <li>* Cut H-Piles to Specified Elevation at South Shore Seawall</li> </ul> | <ul style="list-style-type: none"> <li>* Continue Dewatering South Cofferdam/Pier #22/ Pier#15-#21</li> <li>* Excavation/Up-Keep on South Bank Within the South Seawall Cofferdam</li> <li>* Haul off Excess Spoils Onsite and Store Required Spoils at North Shore Laydown Area</li> <li>* Strip Forms at Abutment #2 Foundation/ Pier #22 &amp; Pier #21</li> </ul> |
|--|---|

#### Next Week Look Ahead

- |  |   |
|--|---|
| <ul style="list-style-type: none"> <li>* Continue Driving H-Piles at South Shore Seawall (Vertical/Battered)</li> <li>* Cut H-Piles to Specified Elevation at South Shore Seawall</li> <li>* Excavate Silt From Around Installed H-Piles Due to Rain Event</li> <li>* Form and Install Steel Reinforcing at South Seawall Foundations</li> </ul> | <ul style="list-style-type: none"> <li>* Continue Dewatering South Cofferdam/Pier #22/ Pier#15-#21</li> <li>* Excavation/Up-Keep on South Bank Within the South Seawall Cofferdam</li> <li>* Install Steel Reinforcing and Form Abutment #2 Wall</li> </ul> |
|--|---|

#### Milestone Events

- |  |  |
|--|--|
| <ul style="list-style-type: none"> <li>* Week of 7/9/18 Pour Pier 21 &amp; 22 TCT Columns</li> </ul> | <ul style="list-style-type: none"> <li>* Week of 7/9/18 Pour West Section of South Shore Seawall Foundation</li> </ul> |
|--|--|

#### Progress Photos

