



Fort Wayne Riverfront Phase 1

Park Foundation Pavilion



Riverfront
FORT WAYNE
Always moving.

Weekly Progress Update for Week Ending 7/15/18

Past Week of Progress

- * Continue Framing/Installation for Ceiling Access Panels Within Event Space
- * Continue Overhead Electrical Rough-In/Lighting Fixture Installation
- * Complete Canopy T&G Soffit Furring
- * Continue Plumbing/Mechanical Wall and Ceiling Rough-In

- * Continue Metal Stud Framing in Pavilion (Event Space Ceiling/Public RR Ceiling)
- * Continue Pex Floor Heat Manifold Connections
- * Continue Installation of Pre-Finished Two Piece Fascia
- * Continue Pre-Finished Metal Flashing at Canopy

Next Week Look Ahead


- * Continue Framing/Installation for Ceiling Access Panels Within Event Space
- * Continue Overhead Electrical Rough-In/Lighting Fixture Installation
- * Start Event Space T&G Soffit Furring
- * Continue Plumbing/Mechanical Wall and Ceiling Rough-In
- * Continue Insulation/Gypsum Board Installation

- * Complete Vestibule Metal Stud Framing
- * Continue Pex Floor Heat Manifold Connections
- * Complete Installation of Pre-Finished Two Piece Fascia
- * Continue Pre-Finished Metal Flashing at Canopy

Milestone Events

- * Seatwall Final Week of 7/23/18

Progress Photos

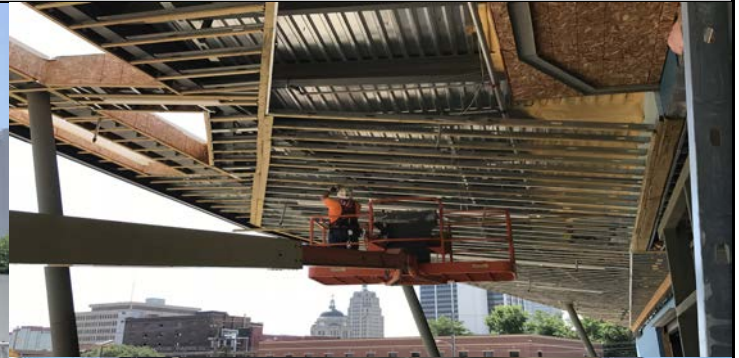



Fort Wayne Riverfront Phase 1

River Work North/South Shore & Misc. Site Excavation



Weekly Progress Update for Week Ending 7/15/18

Past Week of Progress

- * Bring Up Grade to Bottom of South Seawall Footing for First 100' Footing Pour
- * Continue Excavation of Silt From Around Installed H-Piles Due to Rain Event
- * Continue Driving Battered H-Piles at South Shore Seawall
- * Set Up Containment Area for North Cofferdam Spoils Within Laydown Area
- * Backfill Around Pier #21 & Pier #22 TCT Concrete Columns

- * Install Pier #21 & Pier #22 Column Steel Reinforcing, Form, Pour, and Strip Forms
- * Start Excavation of North Seawall Cofferdam (West End)
- * Excavation/Up-Keep on South Bank Within the South Seawall Cofferdam
- * Continue North Seawall Cofferdam Bracing Installation

Next Week Look Ahead

- * Form, Prep, Pour, and Strip Forms for First 100' Footing Section at South Seawall
- * Continue Cutting H-Piles to Specified Elevation Within the South Seawall Cofferdam
- * SPS Mobilization and Start Driving H-Piles Within the North Seawall Cofferdam
- * Pull Sheeting Around Pier #21 & Pier #22 TCT Concrete Columns
- * Reconfigure Pier 15-21 Cofferdam and Install Sheeting Between Pier 20-21

- * Complete H-Pile Installation (Battered Pile) Within South Seawall Cofferdam
- * Bring Up Grade and Form Second Section of Footing for South Seawall
- * Continue Excavation of North Seawall Cofferdam (East End)
- * Continue North Seawall Cofferdam Bracing Installation
- * Excavation/Up-Keep on South Bank Within the South Seawall Cofferdam

Milestone Events

- * Poured TCT Pier #21 & #22 Columns on 7/12/18

- * Week of 7/16/18 Pour First Section of Footing for South Seawall

South Seawall Progress Photos





Fort Wayne Riverfront Phase 1

River Work North/South Shore & Misc. Site Excavation



Weekly Progress Update for Week Ending 7/15/18

North Shore Progress Photos (Parkview TCT & North Seawall)

