



Fort Wayne Riverfront Phase 1 Park Foundation Pavilion



Weekly Progress Update for Week Ending 12/2/18

Past Week of Progress

- * Continue Exterior Canopy T&G Cedar Soffit
- * Continue Installation Wall Tile In Interior Men's and Women's Restroom
- * Sawcut South East/South Exterior Slab at Pavilion Per Design
- * Continue Piping Rough-In Within Rill Equipment Room 114 and Equipment Room 118
- * Continue Detailing Event Space/Concessions Curtain Wall
- * Continue T&G Cedar Siding at Vestibule (Interior)


Next Week Look Ahead

- * Continue Exterior Canopy T&G Cedar Soffit
- * Install Restroom Fixtures in Public Restrooms (Men's 115, Women's 116, Family 117)
- * Install Limestone Cladding at Park Foundation Pavilion Dumpster Enclosure
- * Run Wire making Final Connections for Installed Boilers Within Equipment Room 118
- * Continue Installation of Wall Tile In Interior Men's, Women's, & Family Restrooms
- * Continue Miscellaneous Plumbing Connections Within Equipment Room 114 & 118
- * Continue Detailing Event Space/Concessions Curtain Wall
- * Possible Start on T&G Cedar Ceiling Within P.F. Pavilion Event Space

Milestone Events

- * Week of 12/10/2018 Start Interior T&G Cedar Ceiling Within Pavilion Event Space
- * Week of 12/17/18 Start to Grind and Polish South Half of P.F. Pavilion

Park Foundation Pavilion Progress Photos

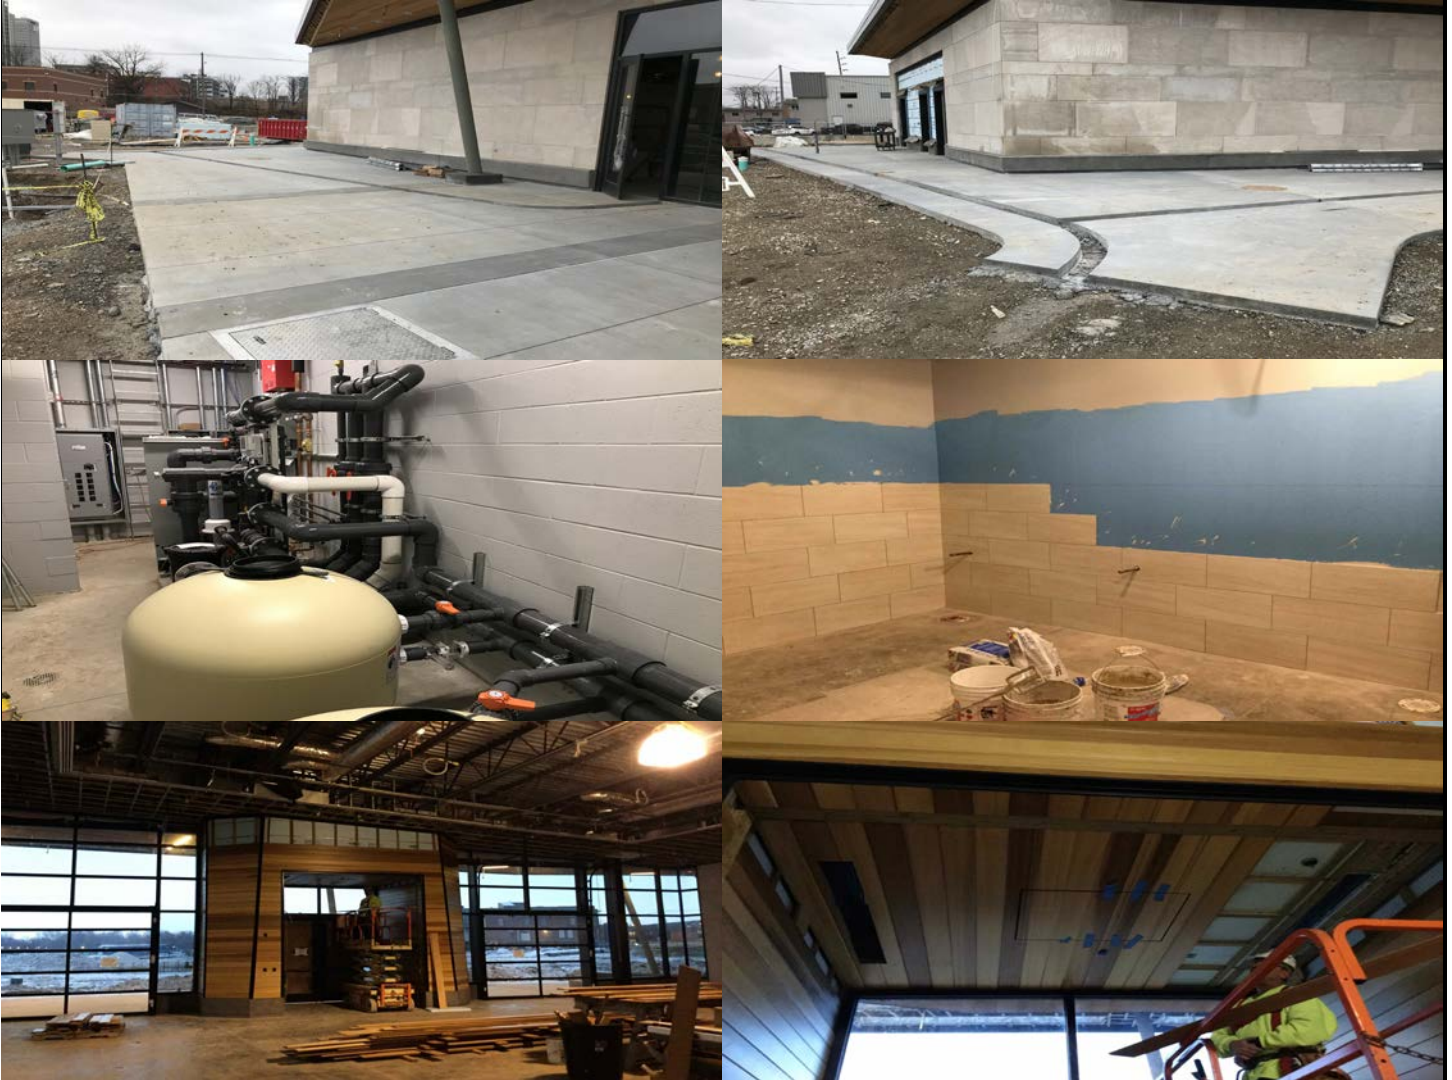



Fort Wayne Riverfront Phase 1

River Work North/South Shore & Misc. Site Excavation



Weekly Progress Update for Week Ending 12/2/18

Past Week of Progress

- * Install Pavers and Tree Grates at Harrison Street ROW
- * Complete Planter Seatwall Foundations at Convergence Sculpture
- * Arkansas Trip for Site and Rill Boulder Selection/Tagging
- * Form, Prep, and Pour Superior Street ROW Sections
- * Miscellaneous Excavation for Electrical and Plumbing Subcontractors
- * Start Installation of IPE on Parkview Tree Canopy Trail Mock-Up

Next Week Look Ahead

- * Backfill South Side of South Seawall For W17 Lounger and W3 Terraced Seating
- * Continue Installation of Pavers at Harrison Street ROW
- * Install Landscaping Sprinkler Lines at Superior ROW
- * Excavate Foundations For Rotary Fountain Near the Weir Gates
- * Install IPE Wood Decking For Parkview TCT Mock-Up
- * Continue to Form, Prep, and Pour Superior Street ROW Sections
- * Continue Installation of 4" PVC Conduit Run from Main Transformer to Secondary
- * Start to Form, Prep, and Pour Sections of Convergence Sculpture Seatwalls
- * Prep and Pour Concrete at Rotary Fountain Near Weir Gates
- * Excavate, Prep, and Pour Concrete For W2 Seating @ Turf and W3 Terraced Seating

Milestone Events

- * Week of 12/3/18 Start Installation of IPE on Parkview Tree Canopy Trail Mock-Up

North/South Site Progress

