



Fort Wayne Riverfront Phase 1 Park Foundation Pavilion



Weekly Progress Update for Week Ending 2/3/19

Past Two Weeks of Progress

- * Complete Interior T&G Cedar Ceiling Within Park Foundation Pavilion Event Space
- * Continue Work on Above Ceiling Electrical in Event Space for Above Ceiling Inspection
- * Install Diffusers Within the Pavilion Event Space
- * Continue Exterior T&G Cedar Soffit on West Side of the Pavilion
- * Start Millwork Installation Within Event Space Bathrooms and Serving Area
- * Receive and Prep Countertops for Event Space Restrooms and Serving Area
- * Continue to Install Restroom Accessories Within Event Space Restrooms


Next Week Look Ahead

- * Start Millwork Installation Within Event Space Bathrooms and Serving Area
- * Complete Exterior T&G Cedar Soffit on West Side of the Pavilion
- * Start installation of Timber Wall Angle Within Event Space
- * Set Countertops for Event Space Restrooms and Serving Area
- * Continue to Install Restroom Accessories Within Event Space Restrooms

Milestone Events

- * Week of 1/28/19 Completed Interior T&G Cedar Ceiling Within Event Space

Park Foundation Pavilion Progress Photos

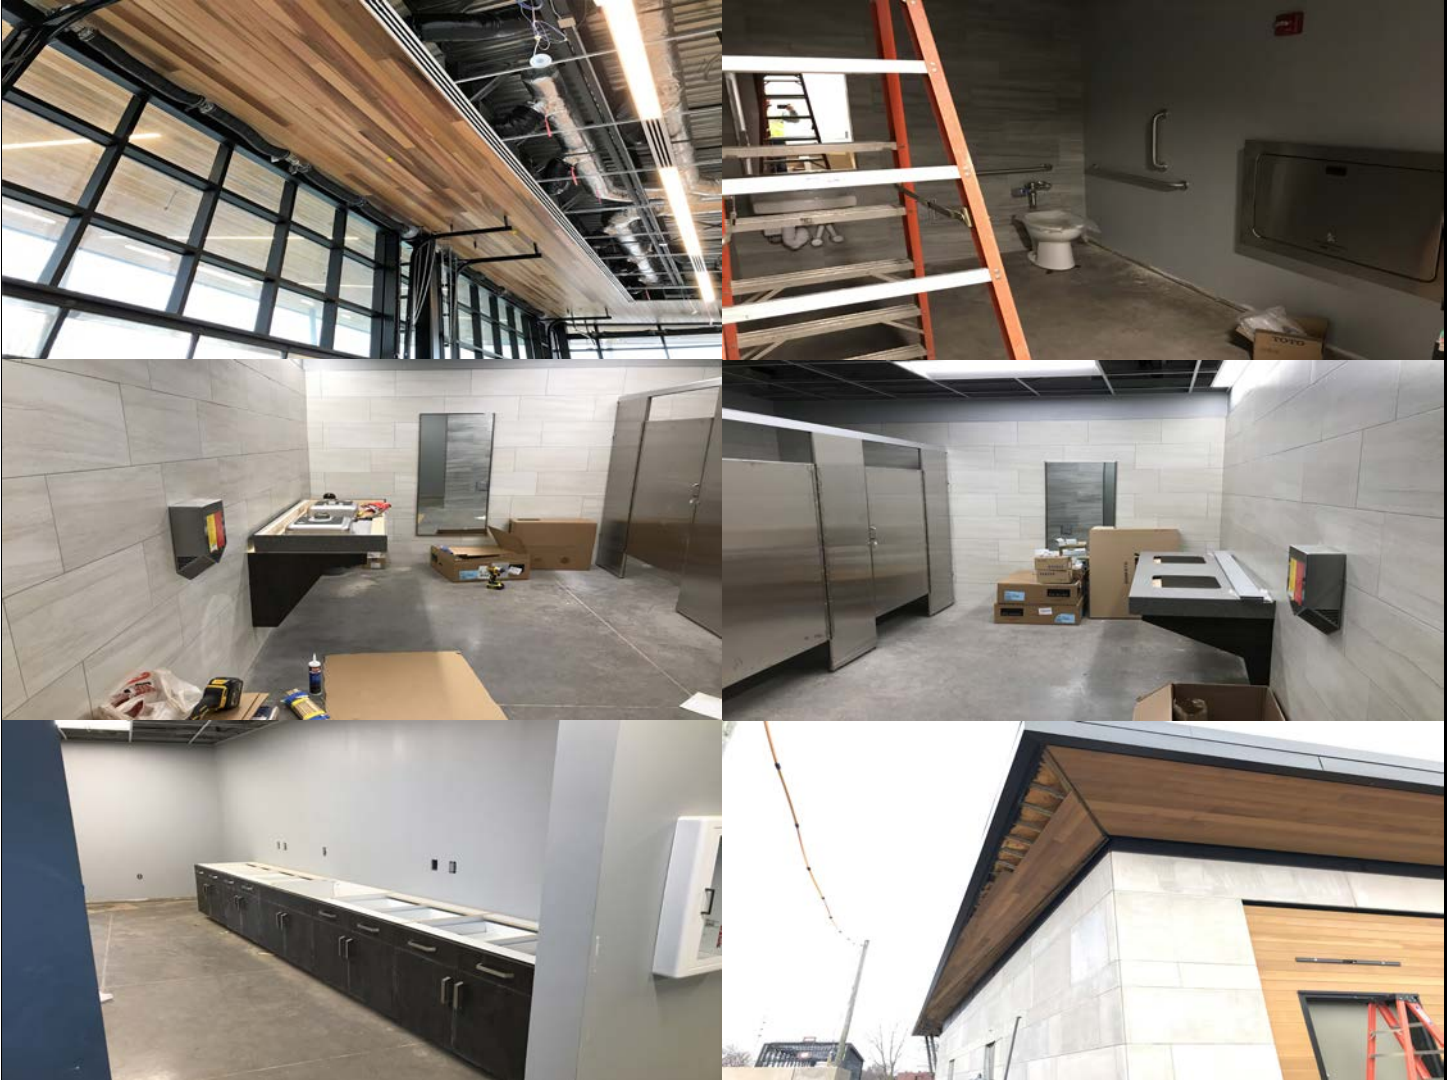



Fort Wayne Riverfront Phase 1

River Work North/South Shore & Misc. Site Excavation



Weekly Progress Update for Week Ending 2/3/19

Past Two Weeks of Progress

- * Demo 2 Specified Trees and Brush on South Bank North of P.F. Pavilion
- * Form South End of Rill at Source Stone and Pour First 12"x6" Curbs @ Kids Canal
- * Pour and Finish W2G West Donor Recognition Seatwall @ Turf
- * Continue to Form 12"x6" Curb Sections at Kids Canal

- * Demo Old Foundation of River Greenway Trail on South Bank
- * Unload 1 Parkview TCT Trail Section and Sweetwater Bandshell Steel
- * Wreck Forms at W2G West Donor Recognition Seatwalls @ Turf & Start Backfill

Next Week Look Ahead

- * Continue Pouring Slab Sections for Kids Canal Water Feature
- * Continue to Form and Pour 12"x6" Curb Sections at Kids Canal
- * Excavate and Install Schedule 80 Pipe for Source Boulder Bubblers
- * Continue to Deck Parkview TCT Trail Sections in North Laydown Area
- * Excavate, Prep, and Pour W2 Planter Seatwall Foundations Throughout Site
- * Form, Prep, and Pour W2D East Donor Recognition Seatwall @ Turf
- * Form, Prep, and Pour W2F West Donor Recognition Seatwall @ Turf

- * Continue to Backfill Behind W2G West Donor Recognition Seatwalls @ Turf
- * Core Boulders for Bubbler PVC Pipe and Place Within K.C. Water Feature for Layout
- * Rework W2/W3 Seating and Continue to Form, Prep, and Pour Additional Sections
- * Set Sweetwater Bandshell Steel Structure
- * Start to Demo Harrison Street Bridge Approaches
- * Excavate, Prep, and Pour W55 West Donor Recognition Seatwalls @ Turf Foundation

Milestone Events

* Week of 1/28/19 Started to Form, Prep, and Pour 12"x6" Rill Curb

* Week of 2/11/19 Start to Form, Prep, and Pour Sweetwater Bandshell Seatwalls

North/South Site Progress

