



Fort Wayne Riverfront Phase 1

Park Foundation Pavilion



Riverfront
FORT WAYNE
Always moving.

Weekly Progress Update for Week Ending 7/22/18

Past Week of Progress

- | | |
|--|---|
| <ul style="list-style-type: none"> * Continue Framing/Installation for Ceiling Access Panels Within Event Space * Continue Overhead Electrical Rough-In/Lighting Fixture Installation * Start Event Space T&G Soffit Furring * Continue Plumbing/Mechanical Wall and Ceiling Rough-In * Continue Insulation/Gypsum Board Installation | <ul style="list-style-type: none"> * Complete Vestibule Metal Stud Framing * Continue Pex Floor Heat Manifold Connections * Complete Installation of Pre-Finished Two Piece Fascia * Continue Pre-Finished Metal Flashing at Canopy |
|--|---|

Next Week Look Ahead

- | | |
|--|---|
| <ul style="list-style-type: none"> * Continue Event Space T&G Soffit Furring * Continue Overhead Electrical Rough-In/Lighting Fixture Installation * Continue Plumbing/Mechanical Wall and Ceiling Rough-In | <ul style="list-style-type: none"> * Insulate and Install Sheathing at Vestibule * Complete Pex Floor Heat Manifold Connections * Continue Pre-Finished Metal Flashing at Canopy |
|--|---|

Milestone Events

- * Seatwall Final Week of 7/23/18

Progress Photos





Fort Wayne Riverfront Phase 1 Park Foundation Pavilion



Weekly Progress Update for Week Ending 7/22/18

Progress Photos (Continued)





Fort Wayne Riverfront Phase 1

River Work North/South Shore & Misc. Site Excavation



Weekly Progress Update for Week Ending 7/22/18

Past Week of Progress

- | | |
|---|---|
| <ul style="list-style-type: none"> * Form, Prep, Pour, and Strip Forms for First 100' Footing Section at South Seawall * Continue Cutting H-Piles to Specified Elevation Within the South Seawall Cofferdam * SPS Mobilization and Start Driving H-Piles Within the North Seawall Cofferdam * Pull Sheeting Around Pier #21 & Pier #22 TCT Concrete Columns * Reconfigure Pier 15-21 Cofferdam and Install Sheeting Between Pier 20-21 | <ul style="list-style-type: none"> * Complete H-Pile Installation (Battered Pile) Within South Seawall Cofferdam * Bring Up Grade and Form Second Section of Footing for South Seawall * Continue Excavation of North Seawall Cofferdam (East End) * Continue North Seawall Cofferdam Bracing Installation * Excavation/Up-Keep on South Bank Within the South Seawall Cofferdam |
|---|---|


Next Week Look Ahead

- | | |
|---|--|
| <ul style="list-style-type: none"> * Prep, Pour, and Strip Forms for Second Section of Footing at South Seawall * Continue Driving Piles Within North Seawall Cofferdam * Pull Sheeting Around Pier #21 TCT Concrete * Start Excavation Within Pier 15-20 Cofferdam | <ul style="list-style-type: none"> * Continue Excavation of North Seawall Cofferdam * Continue North Seawall Cofferdam Bracing Installation * Bring Up Grade/Form Final North Seawall Footing Section * Prep, Form, Pour, and Strip Forms for First Wall Sections at South Seawall |
|---|--|

Milestone Events

- | | |
|---|---|
| <ul style="list-style-type: none"> * Poured First Section of Footing at South Seawall on 7/19/18 | <ul style="list-style-type: none"> * Week of 7/23/18 Pour Second Section of Footing at South Seawall |
|---|---|

South Seawall Progress Photos

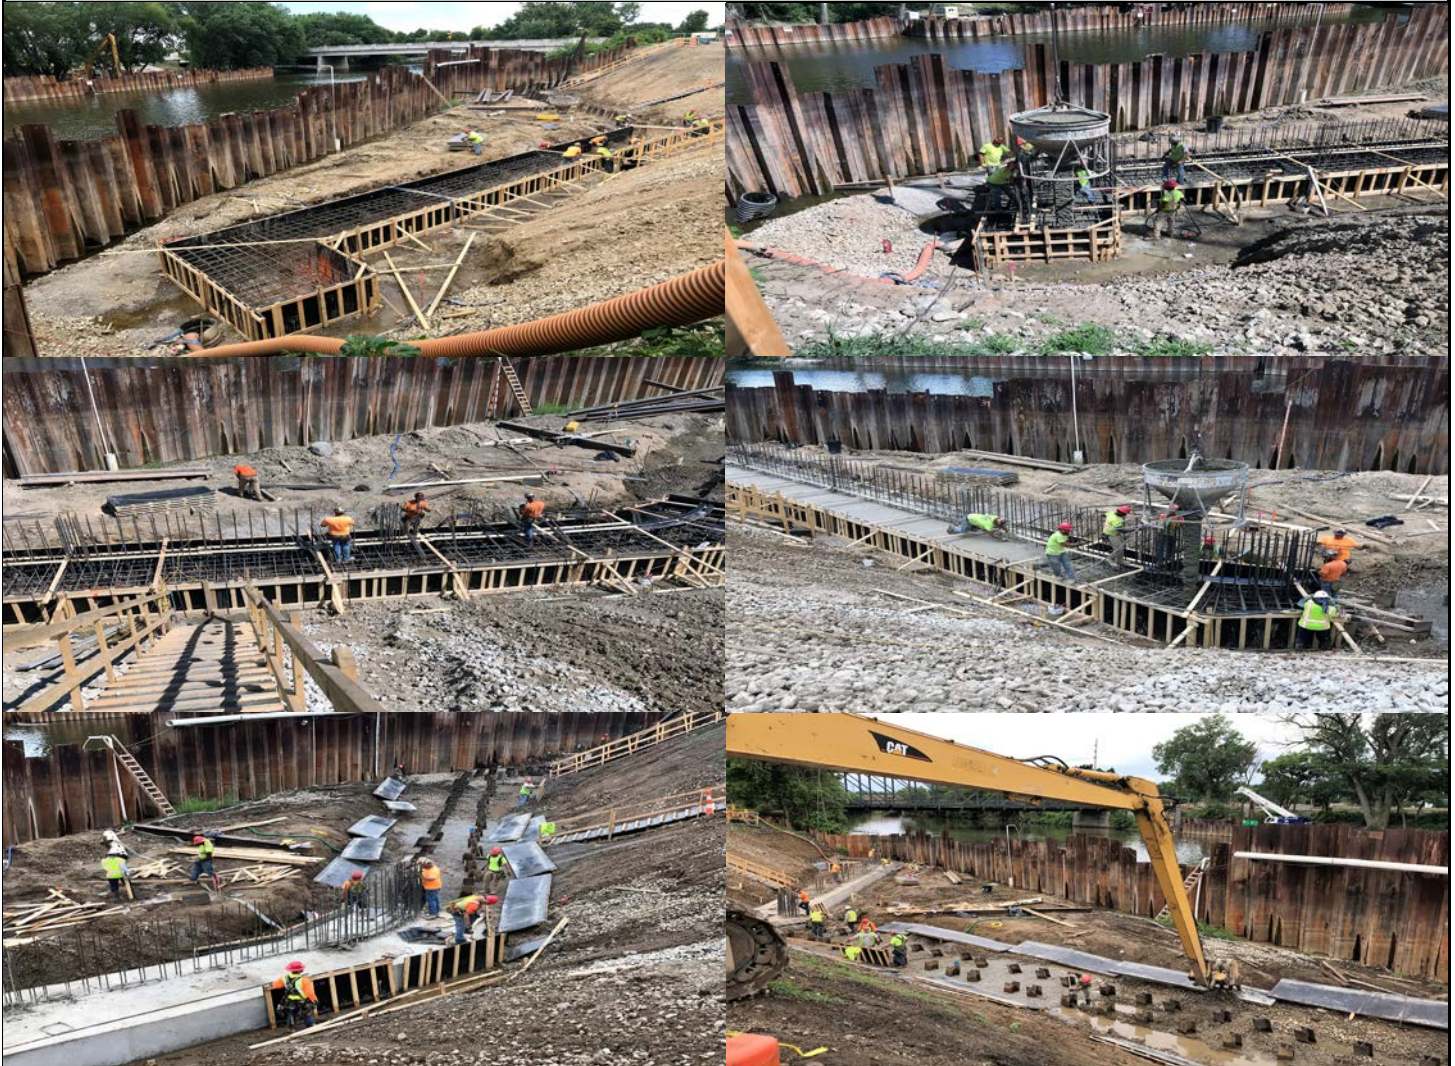



Fort Wayne Riverfront Phase 1 River Work North/South Shore & Misc. Site Excavation



Weekly Progress Update for Week Ending 7/22/18

South Seawall Progress Photos (Continued)



North Shore Progress Photos (Parkview TCT & North Seawall)

