



Fort Wayne Riverfront Phase 1

Park Foundation Pavilion



Riverfront
FORT WAYNE
Always moving.

Weekly Progress Update for Week Ending 8/5/18

Past Week of Progress

- | | |
|--|--|
| <ul style="list-style-type: none"> * Finish Event Space T&G Soffit Furring * Continue Overhead Electrical Rough-In/Lighting Fixture Installation * Continue Plumbing/Mechanical Wall and Ceiling Rough-In * Excavate and Install Concrete Rill Reservoir on East Side of Pavilion * Install Fluid Applied Membrane on Vestibule Sheathing | <ul style="list-style-type: none"> * Insulate and Install Sheathing at Vestibule * Continue Pre-Finished Metal Flashing at Canopy * Grind and Install Densifier on Seat Walls and Curb Walls at Pavilion * Make Plumbing Connections from Pavilion Rill Room to Reservoir * Install Gypsum Board Hard Lid Ceilings at all Public Bathroom Areas |
|--|--|


Next Week Look Ahead

- | | |
|--|---|
| <ul style="list-style-type: none"> * Finish Event Space T&G Soffit Furring * Continue Overhead Electrical Rough-In/Lighting Fixture Installation * Continue Plumbing/Mechanical Wall and Ceiling Rough-In * Mud/Sand All Unfinished Gypsum Board Within the Pavilion | <ul style="list-style-type: none"> * Install Gypsum Board Hard Lid Ceilings at all Public Bathroom Areas * Continue to Grind and Install Densifier on Seat Walls and Curb Walls at Pavilion * Continue to Make Plumbing Connections from Pavilion Rill Room to Reservoir |
|--|---|

Milestone Events

- * Started Seatwall Grinding and Densifier Application on 8/4/18

Progress Photos

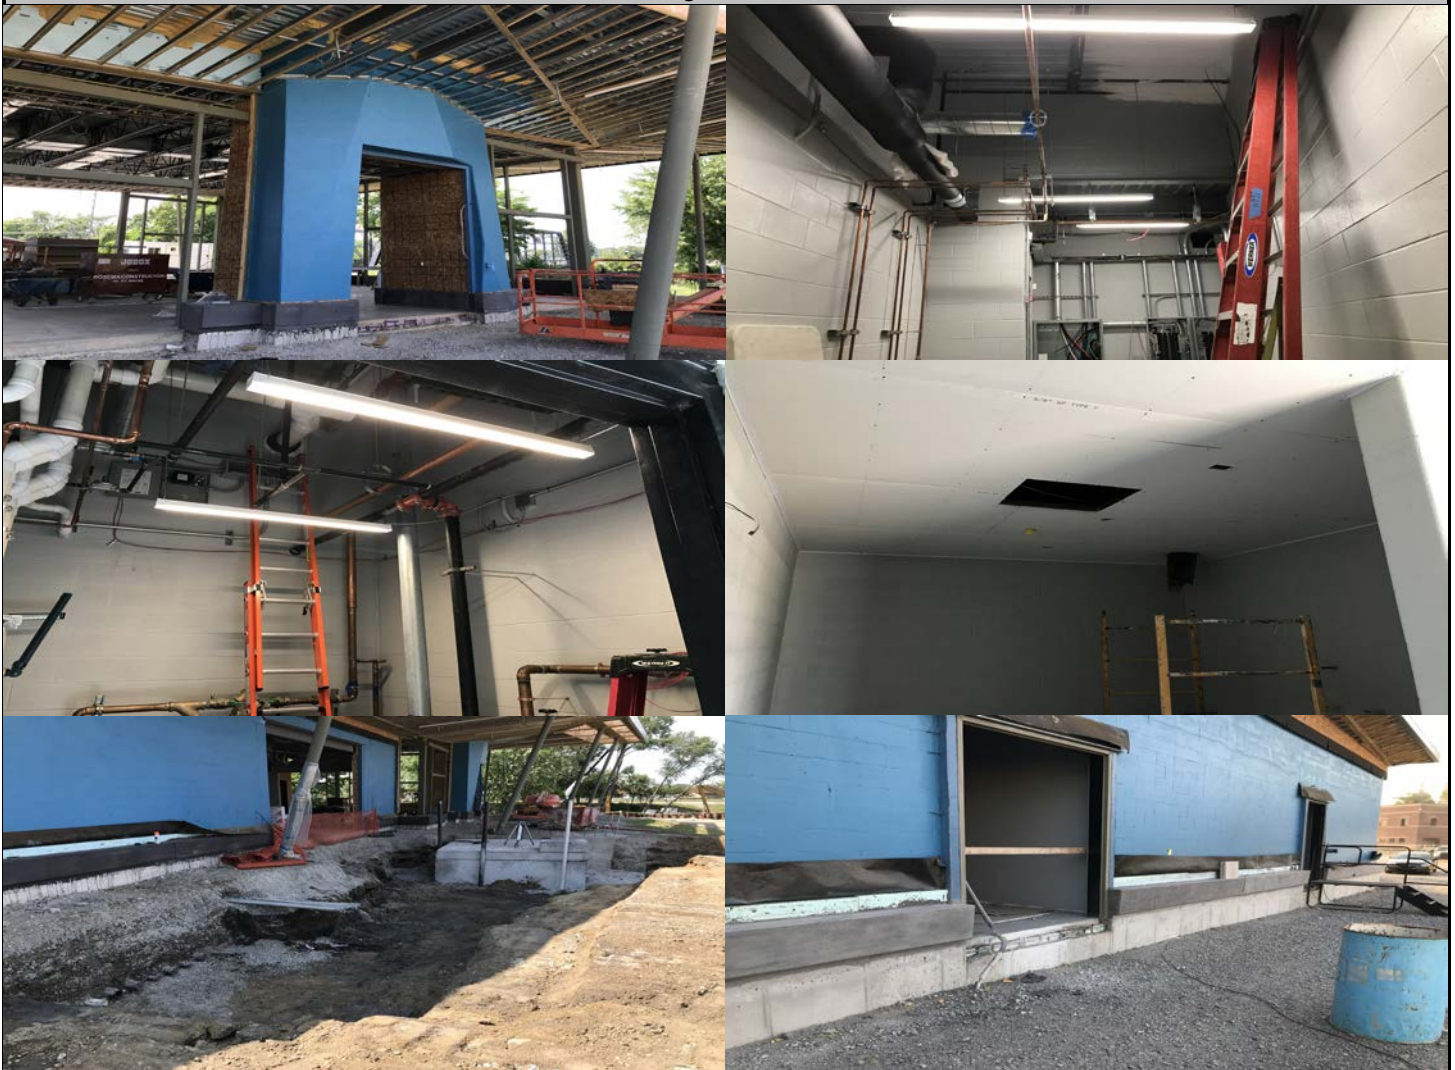



Fort Wayne Riverfront Phase 1

River Work North/South Shore & Misc. Site Excavation



Weekly Progress Update for Week Ending 8/5/18

Past Week of Progress

- * Prep, Pour Concrete, and Strip Forms for Pier #19-#20 Columns
- * Complete Driving Piles Within North Seawall Cofferdam
- * Bring Grade to Bottom of Footing at North Seawall and Start Forming Footing
- * Start Backfill Around Pier 19#-#20 Columns
- * Drive Sheets, Excavate and Drive Vertical/Battered Piles at Abutment #1

- * Complete Excavation of North Seawall Cofferdam
- * Continue North Seawall Cofferdam Bracing Installation
- * Start Excavation and Drive Piles for Pier #5-#7
- * Complete All Wall Section Pours at South Seawall

Next Week Look Ahead

- * Continue Driving Piles and Bring Up Grade to Bottom of Footing at Abutment #1
- * Complete Backfill Around Pier #19-#20 Columns and Pull Sheets at West End
- * Start Excavation of Piers #1-#3 and Drive Vertical/Battered Piles
- * Backfill within #8's at South Seawall and Bring Up to Subgrade

- * Continue to Form, Prep, and Pour North Seawall Footings
- * Reinstall Sheeting on East Side of Pier #19 to Encompass Piers #15-#18
- * Patch Form Ties and Install Self-Adhering Joint Membrane at South Seawall

Milestone Events

* Place Concrete for North Seawall Footings Week of 8/6/18

* Place Concrete for Pier #17-#18 Columns Beginning of Week 8/20/18

South Seawall Progress Photos





Fort Wayne Riverfront Phase 1

River Work North/South Shore & Misc. Site Excavation



Weekly Progress Update for Week Ending 8/5/18

North Shore Progress Photos (Parkview TCT & North Seawall)

